




T8 Dashboard Replication

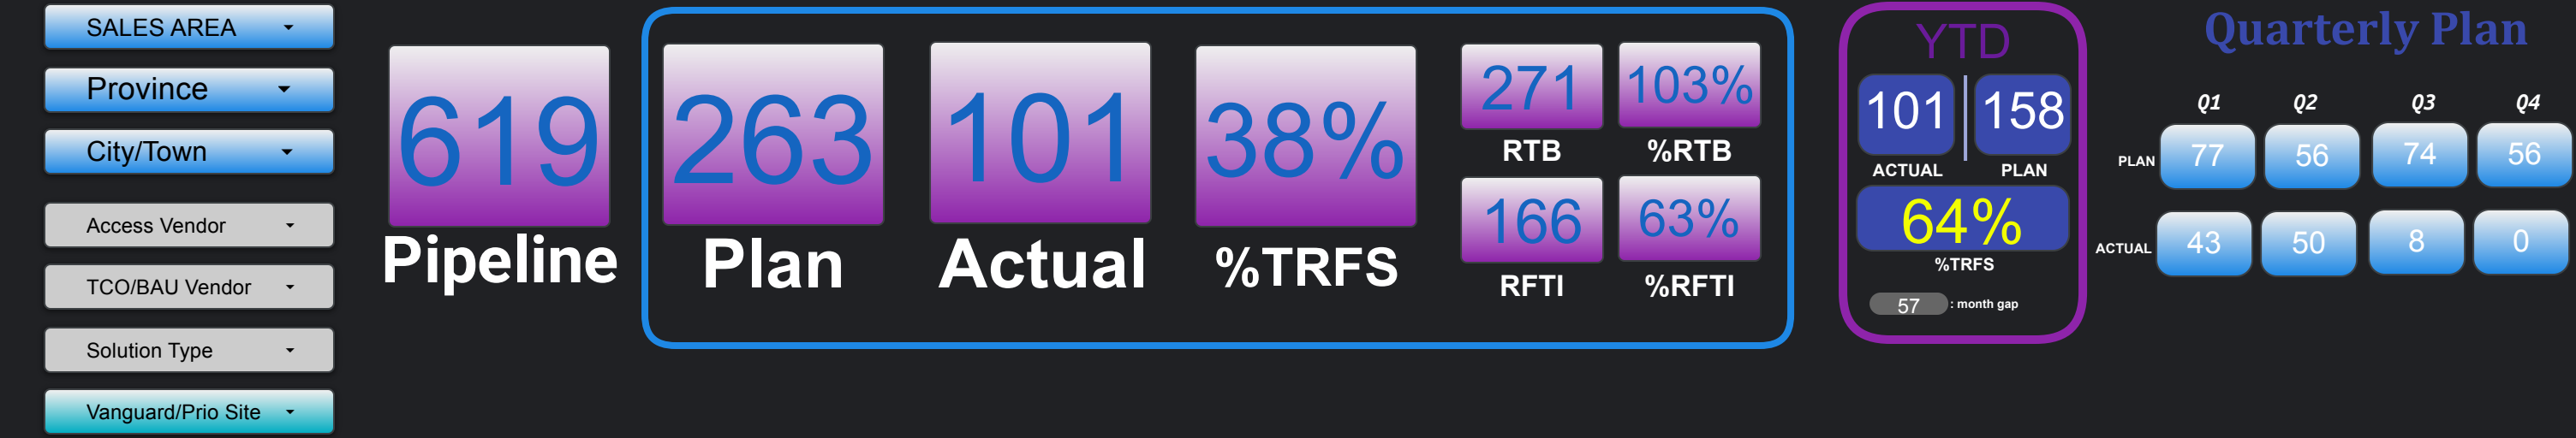


Build Plan

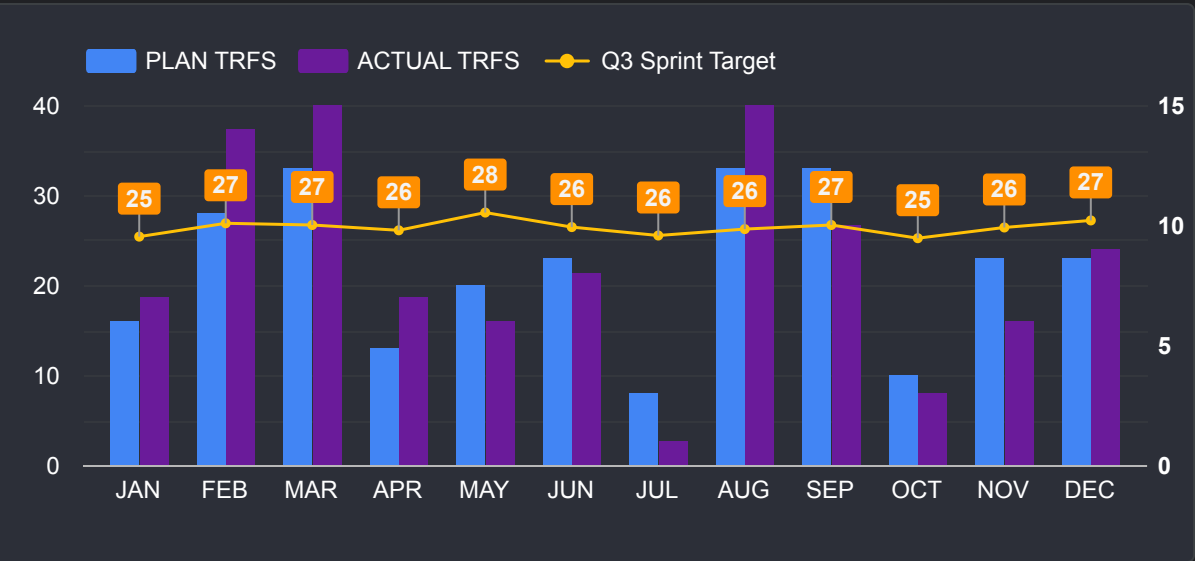

High Level Status

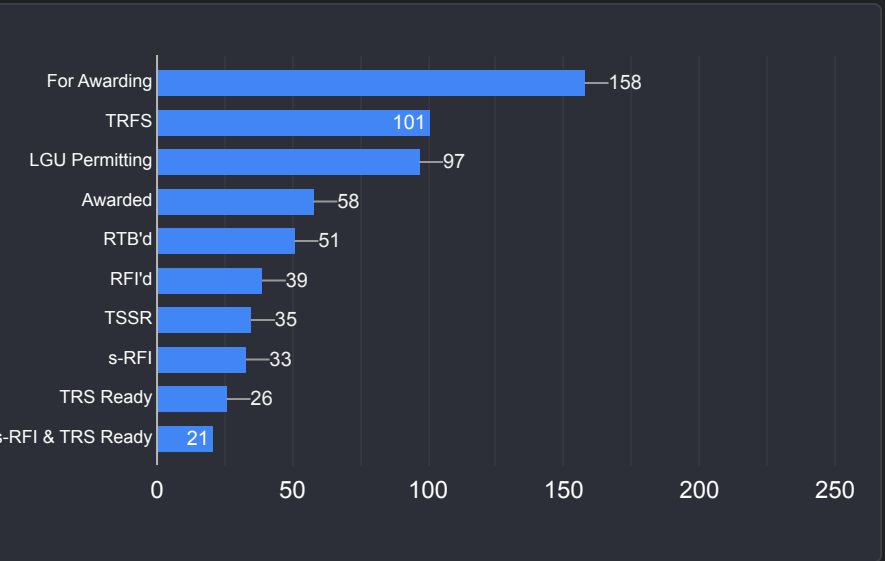


RFI Rally

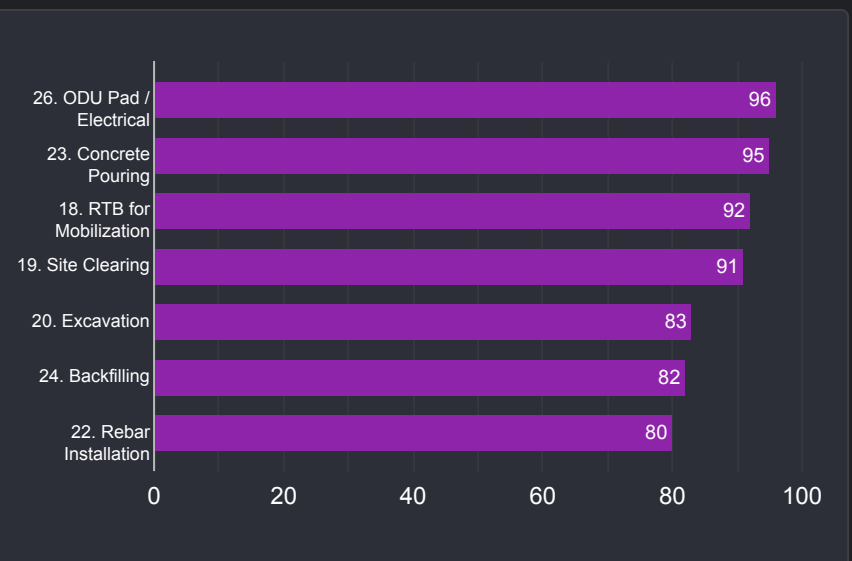

TCO Award and Status


	FRONTIER	PHILTOWER	UNITY	ALLIANCE	LDIC	EDOTCO	ISON
03. For Awarding	58	38	14	19	12	8	2
06. With Issue	8	5	4	2	1	2	1
07. Site Survey	11	5	4	1	1	2	-
14. LC Applied	58	32	19	8	8	7	1
18. RTB for Mo...	19	16	7	5	4	8	-
27. sRFI Pendi...	14	17	3	6	4	1	1
28. sRFI/TRS ...	9	5	3	1	1	-	1
30. RFI/TRS R...	19	12	8	3	2	-	-
32. Ongoing Int...	11	9	3	1	3	2	-
36. TRFS	37	18	9	3	5	10	-

TCO Performance

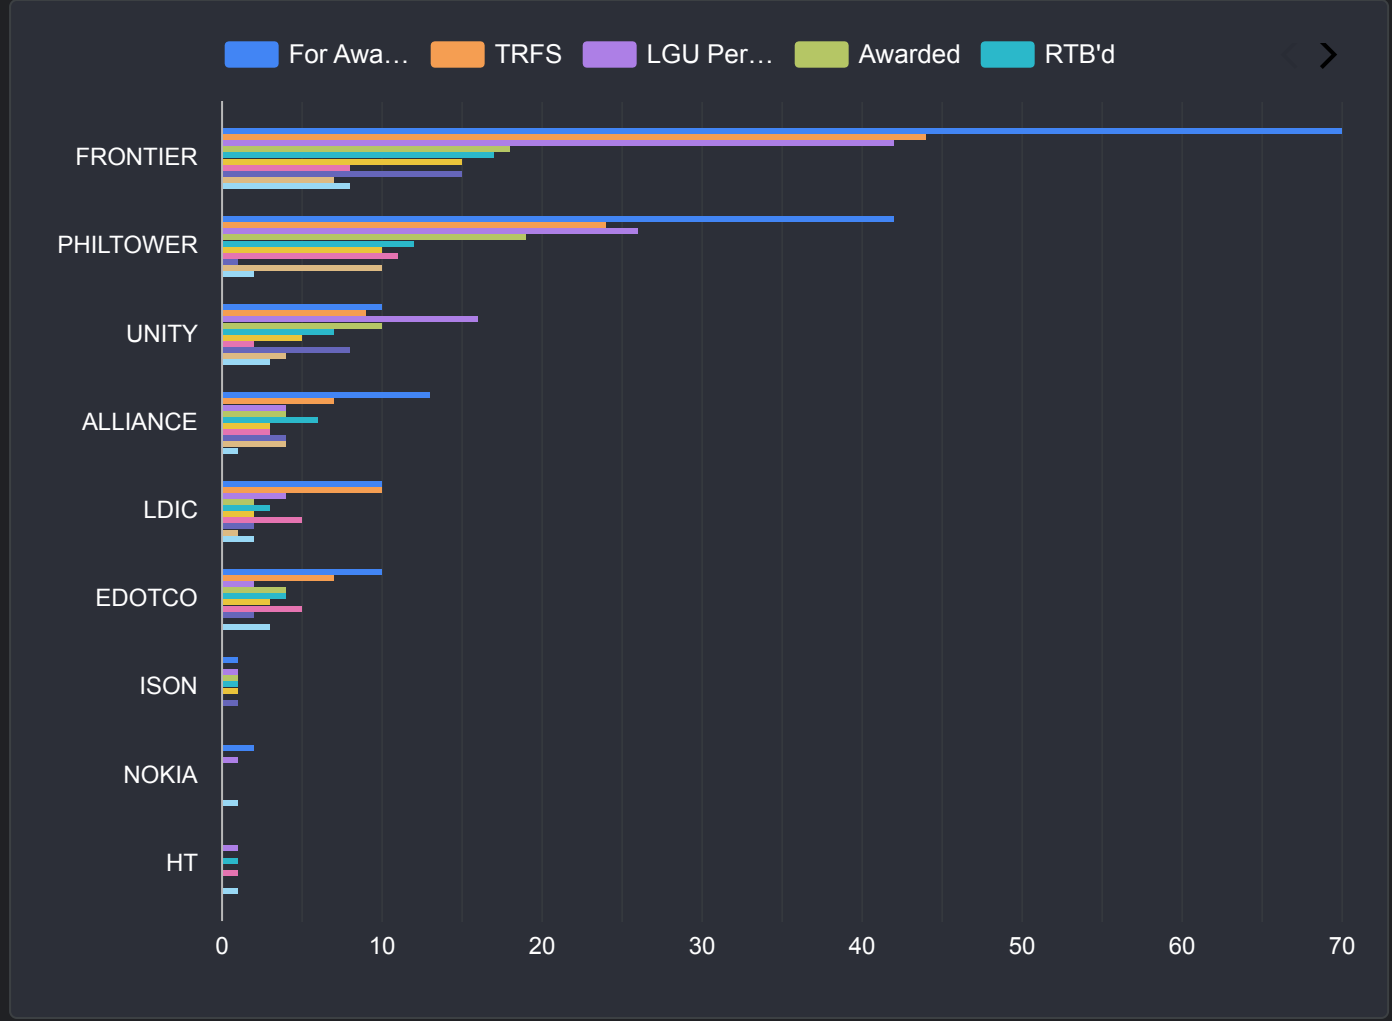

Site Overview

SR Name	SN	High Level Status	Low Level Status
TcoColoc_BrgyLaEsperanza_Tulunan...	NS-TER24-A860	For Awarding	30. RFI/TRS Ready
SR_MIN_DAVAO DEL SUR_DAVAO CIT...	EM2M_NS-TER25-A...	RTB'd	18. RTB for Mobilization
M2SC4_BrgyTambler03_GeneralSantos...	M2SC4-NS-NTG23-D32	LGU Permitting	27. sRFI Pending Pole
M2SC3_BrgyTambler03_GeneralSantos...	M2SC3-NS-NTG23-D32	For Awarding	27. sRFI Pending Pole
M2SC2_BrgyTambler03_GeneralSantos...	M2SC2-NS-NTG23-D32	s-RFI & TRS Ready	27. sRFI Pending Pole
M2SC1_BrgyTambler03_GeneralSantos...	M2SC1-NS-NTG23-D32	For Awarding	27. sRFI Pending Pole
M2EM4_Baymax2020_BrgyMatinaAplay...	M2EM4-NS-BIZ20-G17	RTB'd	18. RTB for Mobilization
Holcim_BrgyIlang_EM_01	NS-NTG23-E38	TSSR	30. RFI/TRS Ready
BrgySisiman_Lutayan_Sultan Kudarat	NS-BIZ22-B66	TRFS	18. RTB for Mobilization
BrgyMankilam02_TagumCity_DDN	NS-NTG23-Q31	For Awarding	27. sRFI Pending Pole
BrgyLa Esperanza_Tulunan_Cotabato (...)	NS-BIZ22-C29	For Awarding	30. RFI/TRS Ready
BrgyDoroluman_Arakan_Cotabato (Nort...	NS-BIZ22-C14	Awarded	18. RTB for Mobilization
BrgyUpperLabay_GeneralSantosCity_S...	NS-NTG23-D61	RTB'd	27. sRFI Pending Pole
BrgyUdtong_Lambayong(MarianoMarco...	NS-TER24-F595	TRFS	18. RTB for Mobilization
BrgyTulunan_DatuAnggalMidtimbang_M...	NS-TER24-E354	TRFS	30. RFI/TRS Ready
BrgySugai01_JoseAbadSantos(Trinidad...	NS-TER24-E798	TRFS	27. sRFI Pending Pole
BrgySanVicente_Asuncion(Saug)_Davao...	NS-TER24-E536	RTB'd	27. sRFI Pending Pole
BrgySanVicente02_PanaboCity_Davao...	NS-TER24-E565	For Awarding	18. RTB for Mobilization
BrgySanIsidro_Lupun_DavaoOriental	NS-TER24-E894	s-RFI	18. RTB for Mobilization
BrgyQuezon_PanaboCity_DavaoDelNorte	NS-TER24-E566	LGU Permitting	18. RTB for Mobilization

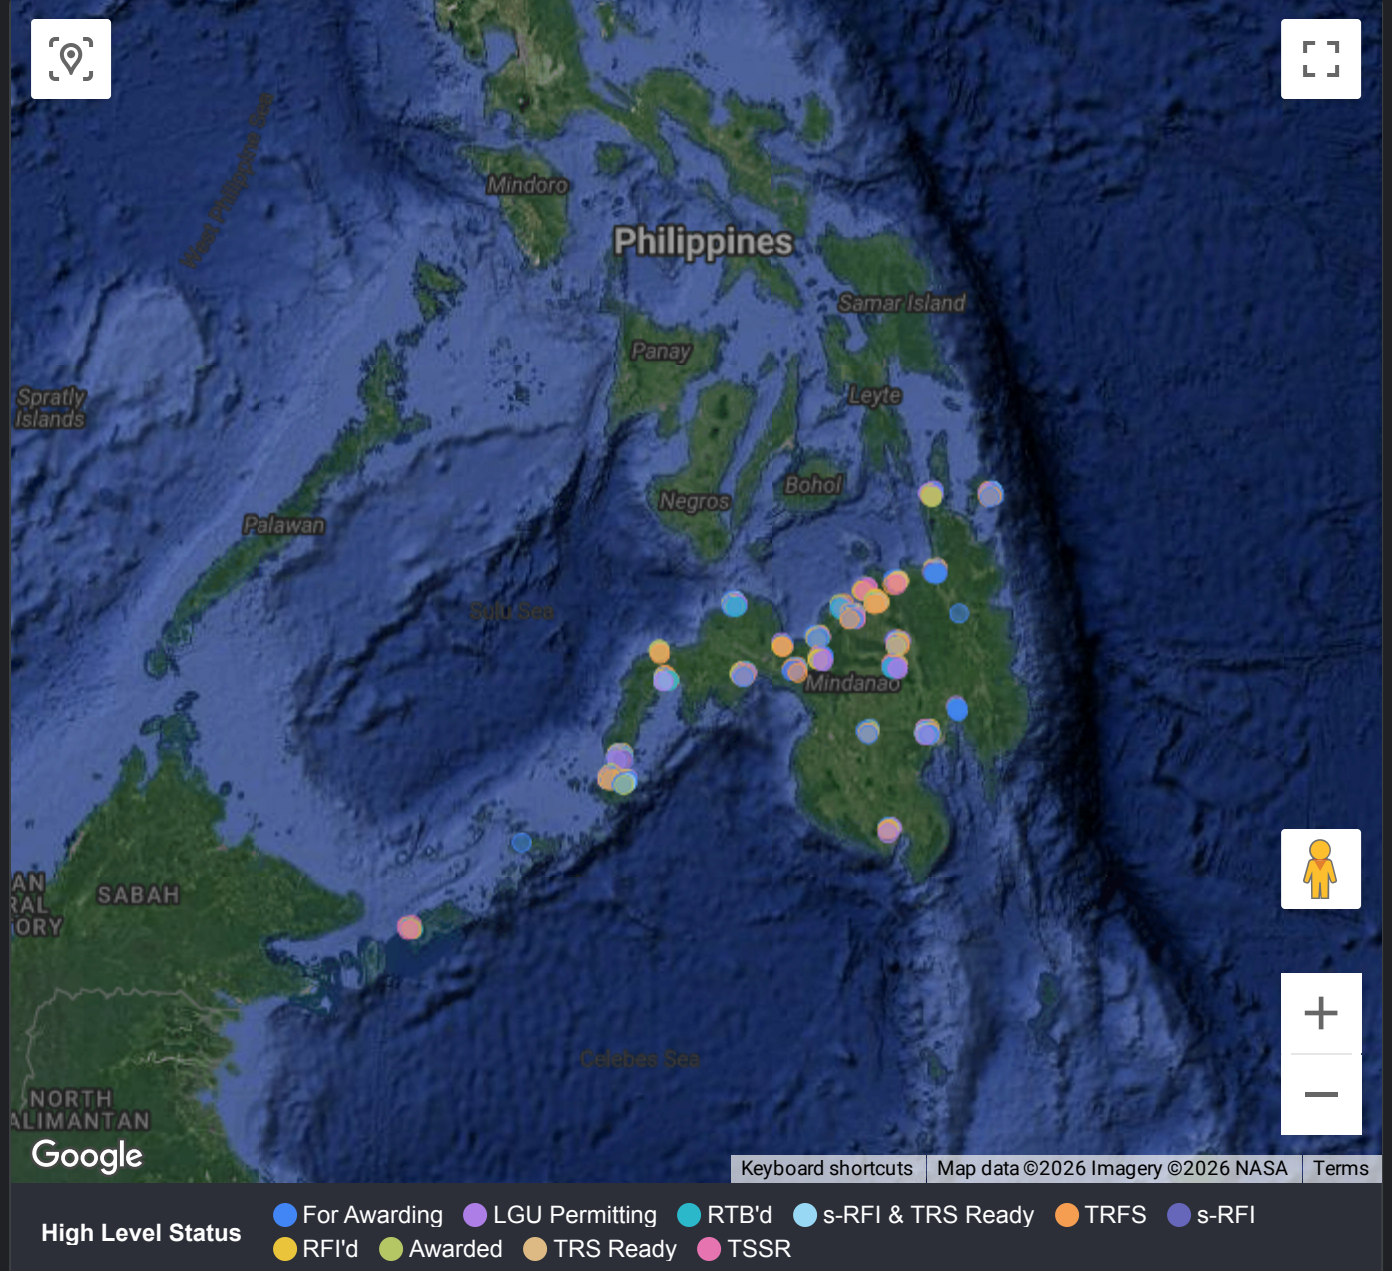

Site Details

High Level Status

SN

SR Name

TCO


Ongoing Wireless Integration (TRS Ready)

SN	SR Name	TCO	TRS Sol'n	TRS Vendor	TRS Actual	Integration Remarks
O234	2022CapSite_BrgyTagMal_Gingogco City	UNITY	Fiber Extension	JISEDAI	Sep 19, 2026	7/21: FOC cut 7/10
B342	2020M2SC2_BrgySanCab_Valencia City	PHILTOWER	MW	JISEDAI	Jun 13, 2026	7/21: FOC cut 7/10
B509	2024M2SC2_BrgyKawMal_Pagadian City (Capital)	FRONTIER	Fiber Extension	HUAXIN	Jan 7, 2026	7/21: FOC cut 7/10
L131	2023M2SC2_BrgyBagBur_Cagayan De Oro City (Capital)	PHILTOWER	MW/FSO	TBD	Mar 3, 2026	7/20: Rftd site 7/15
E174	2023T8_RgPM_BrgyKawDor_Dipolog City (Capital)	FRONTIER	MW/FSO	FADI	Sep 13, 2026	7/20: Rftd site 7/15
D389	2021T8_RgPM_BrgyDorCab_Cagayan De Oro City (Cap...	ALLIANCE	MW	COMTEL	Sep 8, 2026	7/18: Power energized
T927	2021T8_RgPM_BrgyNalLun_Isabela City	PHILTOWER	MW	COMTEL	Dec 1, 2026	7/18: Power energized
D539	2024Capsite_BrgyNalBag_Zamboanga City	ALLIANCE	AN + LEOSAT	HT	Jul 25, 2026	7/05: Integration complete
P529	2020CDNPH_BrgyCabBag_Ipil (Capital)	UNITY	Fiber Extension	TBD	May 8, 2026	7/05: Integration complete
G405	2023CapSite_BrgyBagCab_Cagayan De Oro City (Capital)	UNITY	MW	na	Oct 11, 2026	6/30: Fiber link verified

Ongoing Transport (RFTI'd)

SN	SR Name	Actual RFTI	Lapse	TCO	Access Vendor	ODC	TRS Plan	TRS Sol'n	TRS Ven...
F569	2020T8_RgPM_BrgyLunLib_Cagayan De Oro City (Capital)	Nov 17, 2026	136	FRONTIER	ERICSSON	Nov 7, 2026	Mar 26, 2026	MW/FSO	HUAXIN
C108	2023CDNPH_BrgyLunBag_Zamboanga City	Jan 27, 2026	66	UNITY	ERICSSON	Jan 25, 2026	Jan 23, 2026	Fiber Extension	HT
O986	2020CapSite_BrgyBurMal_Balingasag	Oct 3, 2026	30	ISON	NOKIA	Oct 1, 2026	Nov 7, 2026	AN + LEOSAT	FADI
G624	2022Capsite_BrgyBalKaw_Cagayan De Oro City (Capital)	Oct 8, 2026	80	ALLIANCE	ERICSSON	Nov 20, 2026	Dec 31, 2026	MW/FSO	FADI
B808	2021CapSite_BrgySigNal_Ipil (Capital)	Aug 7, 2026	71	FRONTIER	ERICSSON	Jun 15, 2026	Mar 16, 2026	Fiber Extension	COMTEL
F182	2022M2SC2_BrgyTagBur_Ozamiz City	Feb 28, 2026	144	ALLIANCE	NOKIA	Oct 7, 2026	Apr 13, 2026	AN + LEOSAT	FADI
P602	2021T8_RgPM_BrgyDorLun_Claveria	May 5, 2026	52	EDOTCO	ERICSSON	Oct 10, 2026	Jul 23, 2026	Fiber Extension	JISEDAI
A567	2021CDNPH_BrgyNalDor_Zamboanga City	Jan 27, 2026	64	PHILTOWER	ERICSSON	Feb 3, 2026	Sep 2, 2026	MW/FSO	COMTEL
E694	2021T8_RgPM_BrgySanDor_Zamboanga City	Jul 16, 2026	123	FRONTIER	NOKIA	Jul 15, 2026	Feb 24, 2026	MW/FSO	HUAXIN
B708	2022Capsite_BrgyDorCab_Isabela City	Feb 8, 2026	137	PHILTOWER	ERICSSON	May 16, 2026	Apr 20, 2026	AN + LEOSAT	FADI

Province (Plan vs Actual)

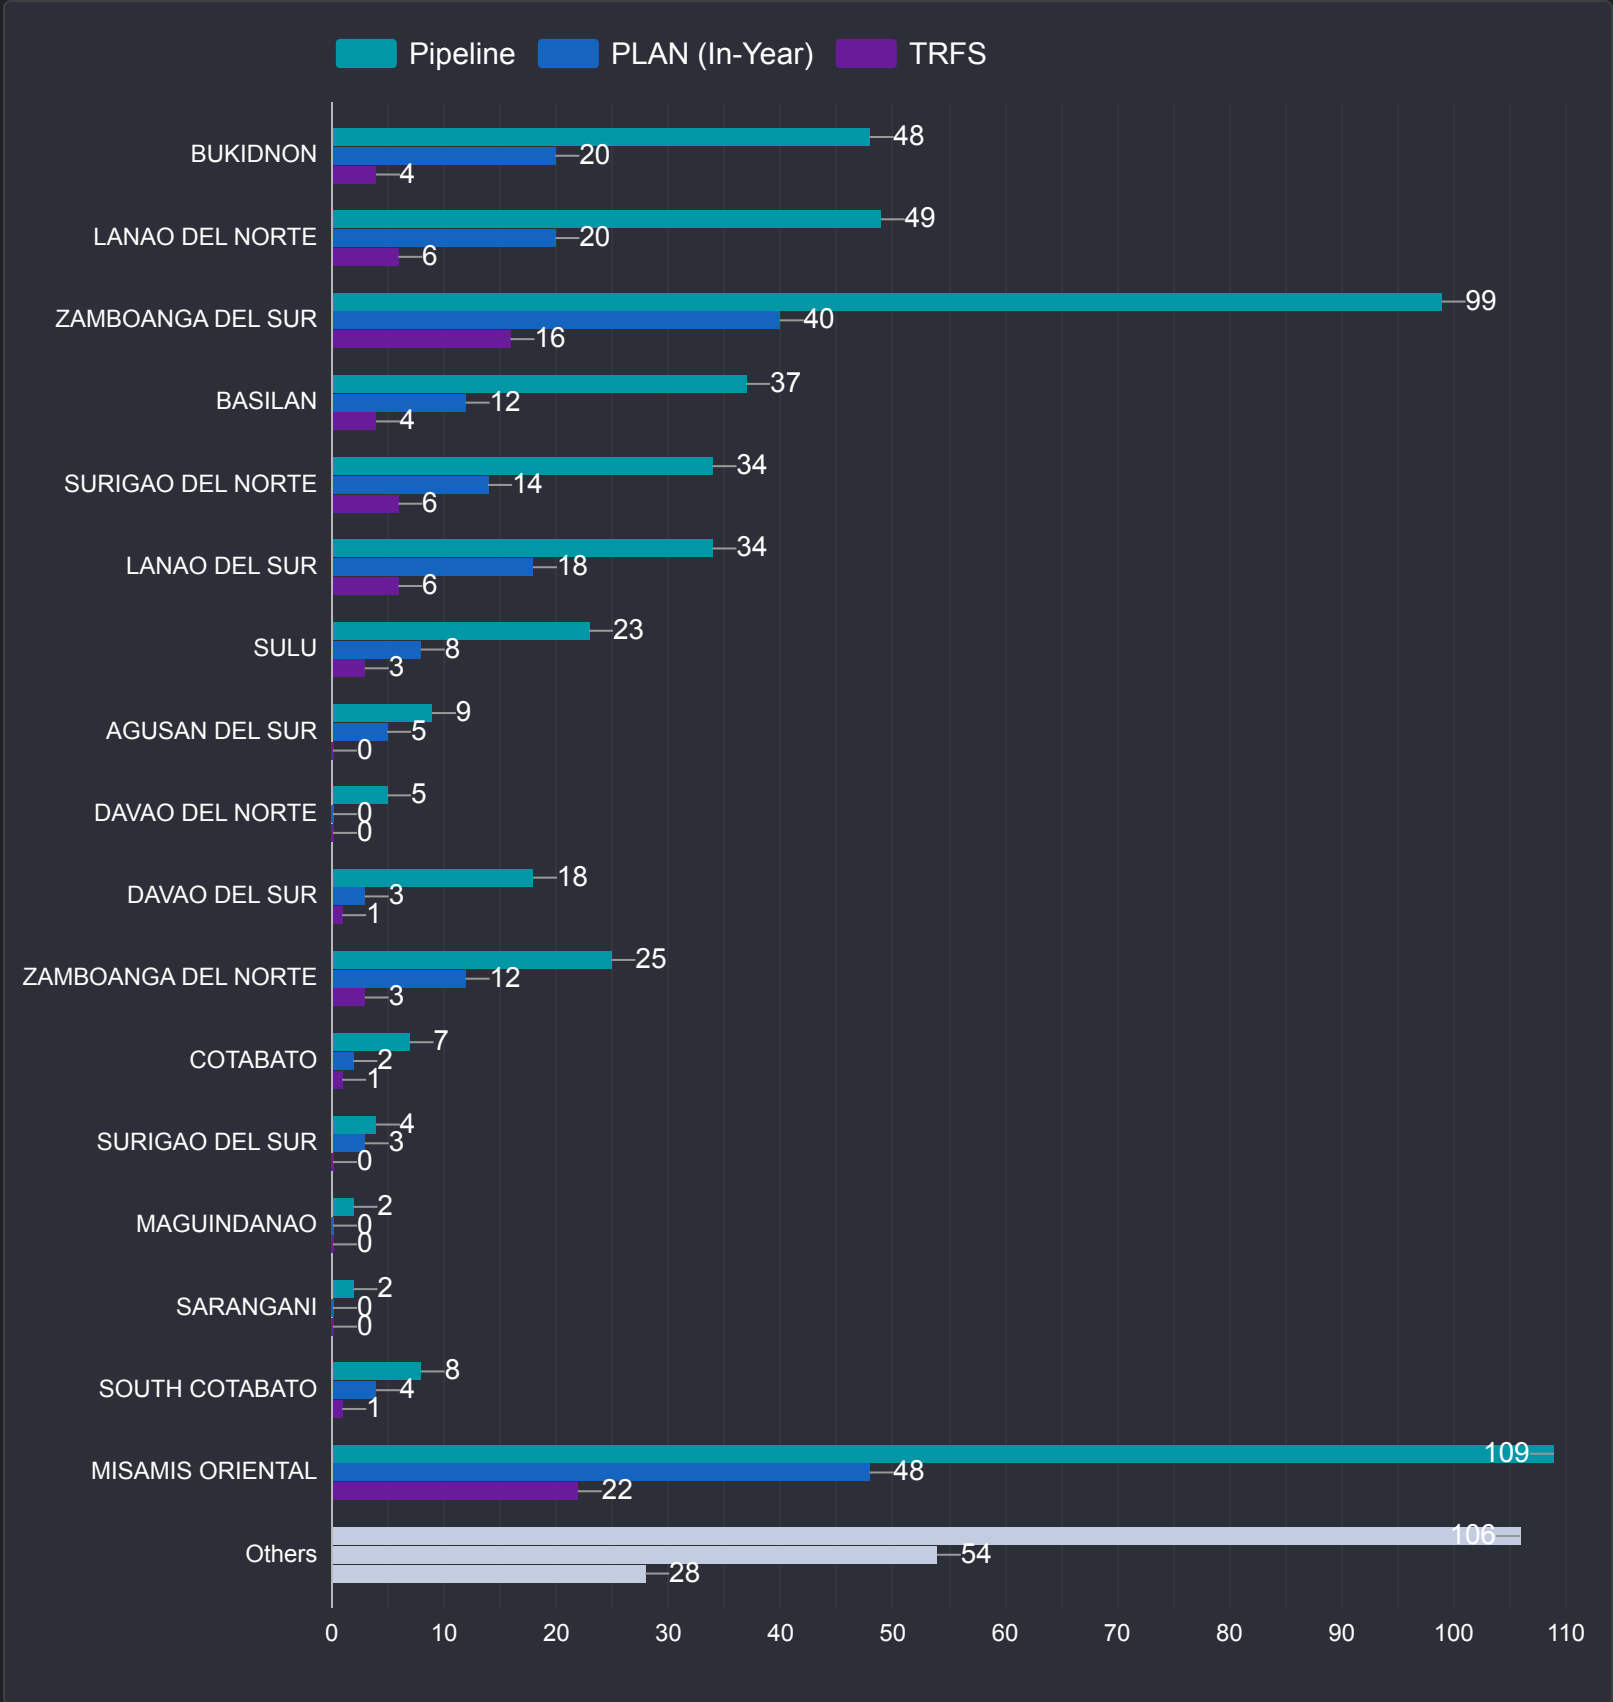

Town (Plan vs Actual)

Town	Pipeline	PLAN (In-Year)	RTB	RFI	TRFS
ZAMBOANGA CITY	130	52	10	7	16
CAGAYAN DE ORO CITY (CAPIT...	110	40	10	9	16
ISABELA CITY	42	21	4	2	10
BUTUAN CITY (CAPITAL)	29	12	2	1	3
DAVAO CITY	25	9	2	3	3
PAGADIAN CITY (CAPITAL)	23	12	1	1	6
DIPOLOG CITY (CAPITAL)	22	8	2	1	1
GENERAL LUNA	22	9	2	0	4
ILIGAN CITY	22	10	1	1	3
VALENCIA CITY	21	14	3	2	4
LAMITAN CITY (CAPITAL)	18	6	1	2	3
MARAWI CITY (CAPITAL)	17	5	0	2	1
MALAYBALAY CITY (CAPITAL)	17	8	0	1	4
IPIL (CAPITAL)	14	9	2	1	5
SURIGAO CITY (CAPITAL)	13	6	1	1	1
CLAVERIA	11	8	1	1	5
GINGOOG CITY	10	3	1	1	2
BALINGASAG	9	3	0	1	0
BONGAO (CAPITAL)	8	4	2	0	3
ARAKAN	7	3	1	0	1
OZAMIZ CITY	7	3	0	1	1
EL SALVADOR CITY	5	3	1	0	1
LABASON	4	1	0	0	1
GENERAL SANTOS CITY	4	3	0	0	0
TULUNAN	3	1	0	0	0

Province (Plan vs Actual)

SN	SR Name	Target RFTI	TCO	CW Status	TRS Vendor	TRS Status	TRS Remarks
T963	2020CDNPH_BrgyNalLun_Valencia City	Nov 28, 2026	PHILTOWER	24. Backfilling	HT	(06) RTB (FOC/AN/Pending)	9/19: Awaiting tower
T927	2021T8_RgPM_BrgyNalLun_Isabela City	Jan 3, 2026	PHILTOWER	26. ODU Pad / Electrical	COMTEL	(00) Not Started	5/20: LOS check passed
T899	2023T8_RgPM_BrgyCabMal_Isabela City	Jul 7, 2026	PHILTOWER	20. Excavation	TBD	(05) Permitting	01 Precon/ Eng'g Hold
T849	2023Capsite_BrgyTagBur_Lamitan City (Capital)	Dec 25, 2026	EDOTCO	22. Rebar Installation	TBD	(01) Precon/ Eng'g Hold	6/24: for checking
T834	2020M2SC2_BrgyDorkKaw_Zamboanga City	Dec 22, 2026	FRONTIER	19. Site Clearing	TBD	(02) Survey	3/31: Brgy Permit S
T79	2023Capsite_BrgyBagSan_Cagayan De Oro City (Capital)	Mar 2, 2026	FRONTIER	19. Site Clearing	TBD	(06) RTB (FOC/AN/Pending)	01 Precon/ Eng'g Hold
T789	2022CDNPH_BrgyBagSan_El Salvador City	Apr 2, 2026	FRONTIER	22. Rebar Installation	NOKIA	(02) Survey	7/02: FOC splicing ongoing
T770	2022Capsite_BrgyMalDor_Davao City	Apr 18, 2026	LDIC	19. Site Clearing	COMTEL	(00) Not Started	9/19: Awaiting tower
T768	2023CDNPH_BrgyBalMal_Davao City	Apr 9, 2026	UNITY	26. ODU Pad / Electrical	ZTE	(05) Permitting	6/24: for checking
T720	2022M2SC2_BrgyLibBag_Zamboanga City	Dec 25, 2026	FRONTIER	18. RTB for Mobilization	na	(01) Precon/ Eng'g Hold	6/15: MW dish installed
T706	2022M2SC2_BrgyBurLib_Butuan City (Capital)	Feb 23, 2026	ALLIANCE	19. Site Clearing	ZTE	(00) Not Started	6/24: for checking
T694	2020T8_RgPM_BrgyBalMal_Zamboanga City	Dec 5, 2026	UNITY	26. ODU Pad / Electrical	na	(02) Survey	6/24: for checking
T69	2021CapSite_BrgyBagMal_Cagayan De Oro City (Capital)	Dec 3, 2026	PHILTOWER	19. Site Clearing	NOKIA	(06) RTB (FOC/AN/Pending)	5/20: LOS check passed
T689	2022M2SC2_BrgyCabMal_Iligan City	Jan 24, 2026	FRONTIER	22. Rebar Installation	HT	(05) Permitting	06 RTB (FOC/ AN/ ...
T636	2020Capsite_BrgySigDor_Bongao (Capital)	Aug 5, 2026	EDOTCO	18. RTB for Mobilization	JISEDAI	(01) Precon/ Eng'g Hold	6/24: for checking
T624	2021Capsite_BrgyTagCab_Pagadian City (Capital)	Nov 28, 2026	PHILTOWER	20. Excavation	ZTE	(05) Permitting	9/19: Awaiting tower
T592	2022T8_RgPM_BrgyKawSan_Zamboanga City	Aug 22, 2026	PHILTOWER	20. Excavation	TBD	(02) Survey	6/24: for checking
T59	2020T8_RgPM_BrgyBurDor_Pagadian City (Capital)	Jul 9, 2026	FRONTIER	26. ODU Pad / Electrical	na	(00) Not Started	12/10: no pole yet
T557	2023T8_RgPM_BrgyBagCab_Davao City	Nov 28, 2026	FRONTIER	19. Site Clearing	HT	(01) Precon/ Eng'g Hold	9/19: Awaiting tower
T548	2022M2SC2_BrgyCabTag_Cagayan De Oro City (Capital)	Oct 14, 2026	FRONTIER	19. Site Clearing	COMTEL	(01) Precon/ Eng'g Hold	10/17: Pending site
T541	2021M2SC2_BrgyLunLib_General Luna	Aug 13, 2026	FRONTIER	24. Backfilling	na	(01) Precon/ Eng'g Hold	6/15: MW dish installed
T538	2024T8_RgPM_BrgyLunLib_Valencia City	Sep 4, 2026	PHILTOWER	26. ODU Pad / Electrical	ZTE	(05) Permitting	12/10: no pole yet
T528	2023CapSite_BrgyLibDor_El Salvador City	Feb 24, 2026	FRONTIER	23. Concrete Pouring	HT	(02) Survey	06 RTB (FOC/ AN/ ...
T50	2023CapSite_BrgyBagNal_Lamitan City (Capital)	Jul 11, 2026	UNITY	19. Site Clearing	JISEDAI	(06) RTB (FOC/AN/Pending)	01 Precon/ Eng'g Hold
T485	2023CDNPH_BrgyBalSan_Dipolog City (Capital)	Mar 9, 2026	UNITY	20. Excavation	na	(05) Permitting	12/10: no pole yet
